

AEE O & M SUB DVN-4 HESCOM, NAVANAGAR, HUBLI

&

THE REGISTRAR KARNATAKA LAW UNIVERSITY HOSTEL BUILDING, NAVANAGAR

The Registrar Karnataka Law University Hostel Building, Navanagar is the consumer of HESCOM located at The Registrar Karnataka Law University Hostel Building, Navanagar, hereinafter referred to as the "Seller" (which expression shall, unless repugnant to the context or meaning thereof, include its successors and permitted assigns) as part of the second part.

Whereas,

The HESCOM, with consent of Seller intends to install/has installed without any cost to the Seller, a SRTPV system of 48kWp capacity on the roof top of the premises situated at The Registrar Karnataka Law University Hostel Building, Navanagar and connected to electricity service connection bearing number [RR. No]/ACC.ID. 9381396129 having sanctioned load of 32.2KW in the same premises under NAVANAGAR SECTION OFFICE O& M SUB DVN-4, NAVANAGAR HESCOM.

Now therefore, in consideration of the foregoing premises, the parties hereto, intending to be legally bound hereby agree as under:

1. Technical and Interconnection Requirements:

1.1 SRTPV system shall be designed, engineered, constructed and operated and also maintained for the duration of this agreement by the HESCOM with reasonable diligence subject to all applicable Indian laws, Rules, Regulations as amended, from time to time and orders having the force of law.

1.2 HESCOM shall ensure that the SRTPV system complies with all the technical and interconnection requirement in terms of the KERC (Implementation of Solar Rooftop Photovoltaic Power Plants) Regulations, 2016, as amended from time to time.

2. Safety:

The HESCOM and Seller shall comply with the safety measures in terms of the KERC (Implementation of Solar Rooftop Photovoltaic Power Plants) Regulations, 2016 as amended from time to time.

2.1 The HESCOM and Seller shall comply with the Central Electricity Authority (Measures Relating to Safety and Electricity Supply) Regulations 2010.

2.2 If the Seller's SRTPV system either causes damage to and/or produces adverse effects on the other consumers' or HESCOM's assets, HESCOM will disconnect SRTPV system immediately from the distribution system and rectify the same HESCOM own cost before reconnection.

3. Clearances and Approvals:

The HESCOM on behalf of the Seller shall obtain any statutory approvals and clearances that may be required, such as from the Electrical Inspector or the municipal or other authorities, before connecting the Roof-top Solar PV System to the grid/distribution system.

4. Access and Disconnection:

4.1 HESCOM shall have access to metering equipment and disconnecting device of SRTPV system, both automatic and manual, at all times.


4.2 In emergency or outage situation, where there is no access to a disconnecting device either automatic or manual, the HESCOM shall have the right to disconnect power supply to the premise.

5. Liabilities:

5.1 The HESCOM shall be solely responsible for availing any fiscal or other incentive provided by the State/ Central government, at his own expenses.

Karnataka Electricity Regulatory Commission


IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.


Registrar
Karnataka State Law University
Navanagar, Hubballi-580 025.

Page no- 2

10. The Seller & HESCOM jointly agree to maintain the SRTPV installation in good condition for period of 25 years being the useful life of the plant. The HESCOMs agree to bare any cost of the SRTPV installation for the useful life of the plant including any cost towards maintenance of the SRTPV plant for the useful life of the plant.








11. Dispute Resolution:

11.1 All the disputes between the parties arising out of or in connection with this agreement shall be first tried to be settled through mutual negotiation.

11.2 The parties shall resolve the dispute in good faith and in equitable manner.

11.3 In case of failure to resolve the dispute, either of the parties may approach the Commission for its resolution.

IN WITNESS WHEREOF, the Seller and the HESCOM have entered into this Agreement executed on the date and year first set forth above. For AND ON BEHALF OF HESCOM.

<p>HESCOM: By:  Designation: Assistant Executive Engineer Address: Q & M City Sub-Division-4 Mobile number: Navanagar, HUBBALLI-580 025</p>	<p>SELLER: By: The Registrar Karnataka law University Hostel Building, Navanagar RR No/AC ID :9381395129 Address:  Registrar Mobile number: Karnataka State Law University Navanagar, Hubli-25.</p>
<p>1. WITNESS In Presence of Name:  Designation: ಶಾಖಾ ಅಧಿಕಾರಿಗಳು ನವನಗರ ಶಾಖೆ ಕು.ವಿ.ಸ.ಕಂ. ನವನಗರ, ಹುಬ್ಬಳ್ಳಿ Mobile number :</p>	<p>1. WITNESS In Presence of Name:  Address: Resident Engineer Karnataka State Law University Navanagar, Hubli - 580025 Mobile number :</p>
<p>2. WITNESS In Presence of Name:  Designation:  Mobile number :</p>	<p>2. WITNESS In Presence of Name:  Address: 06/09/2019 Mobile number : Assistant Engineer</p>

Karnataka Electricity Regulatory Commission

END.


IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.


Registrar
Karnataka State Law University
Navanagar, Hubballi-580 025.

KEB Bill Details for the year 2018-19

Sl. No.	Name of the Building	R/R No. / A/c No.	April	May	June	July	August	September	October	November	December	January	February	March
1	CDC, DSW, Legal Cell & NSS Sections	26032A / 20774251000	1,898.00	1,120.00	479.00	759.00	616.00	718.00	794.00	298.00	546.00	535.00	603.00	1,009.00
2	New Guest House Building	437126 / 6483149550	4,338.00	4,179.00	2,748.00	5,158.00	4,576.00	4,791.00	5,761.00	5,374.00	7,747.00	6,999.00	7,336.00	9,963.00
3	Parabeta Bhavan	/ 9599801106	16,624.00	25,120.00	-	15,907.00	14,211.00	13,089.00	14,345.00	12,638.00	12,002.00	12,876.00	12,883.00	14,792.00
4	New Law School Building	HT-583 / 9797263467	-	-	-	-	-	-	-	-	34,838.00	34,536.00	31,814.00	36,381.00
5	Ladies Hostel	/ 9381346129	35,874.00	37,093.00	32,399.00	20,097.00	35,719.00	40,481.00	40,435.00	47,001.00	42,968.00	21,175.00	34,998.00	42,421.00
6	Administrative Building	73074C / 2180851000	55,499.00	52,227.00	41,019.00	37,368.00	43,194.00	41,610.00	55,818.00	32,693.00	40,439.00	35,616.00	33,758.00	51,314.00
7	Pump House	MP8809 / 3960061000	2,918.00	-	-	-	-	-	-	-	-	-	-	1,398.00
Sub Total			1,17,061.00	1,19,739.00	76,545.00	79,686.00	98,316.00	1,00,689.00	97,103.00	93,734.00	1,38,538.00	1,11,717.00	1,21,454.00	1,57,278.00
Grand Total			1311875.00											


IQAC COORDINATOR
 Karnataka State Law University
 Hubballi-25.


Registrar
 Karnataka State Law University
 Ponnagan, Hubballi-580 025.

KSEB Bill Details for the year 2019-20

Sl No.	Name of the Building	HR. No. / A/c No.	April	May	June	July	August	September	October	November	December	January	February	March
1	COO, DSW, Legal Cell & NSS Sector	2601A / 207745100	750.00	965.00	607.00	1,262.00	1,398.00	925.00	-	-	5,436.00	1,794.00	1,809.00	-
2	New Guest House Building	477120 / 1485549550	7,883.00	18,791.00	6,827.00	5,780.00	5,449.00	6,022.00	-4,623.00	5,407.00	5,265.00	3,092.00	7,381.00	-
3	Parvathi Bhavan	/ 9599801106	13,323.00	14,718.00	10,748.00	13,928.00	15,247.00	9,997.00	13,913.00	13,044.00	12,951.00	14,964.00	14,195.00	13,818.00
4	New Law School Building	HT-303 / 9797303487	38,898.00	34,504.00	56,381.00	32,725.00	37,744.00	38,602.00	37,025.00	33,718.00	99,387.00	37,189.00	36,331.00	38,917.00
5	Lalita Hotel	/ 9381296129	42,421.00	46,487.00	47,478.00	25,011.00	27,294.00	2,385.00	-	-	7,494.00	-	-	-
6	Administrative Building	730794 / 2189810000	38,373.00	42,178.00	26,031.00	32,781.00	-	-	-	-	-	-	-	-
7	Pump House	M78808 / 5500001000	-	-	-	-	-	-	-	-	-	1,012.00	3,861.00	-
Sub Total			1,43,445.00	1,51,551.00	1,41,332.00	1,11,494.00	87,966.00	57,932.00	85,563.00	-1,589.00	1,23,483.00	96,997.00	82,813.00	92,755.00
Grand Total			1094377.00											


IQAC COORDINATOR
 Karnataka State Law University
 Hubballi-25.


Registrar
 Karnataka State Law University
 Navanagar, Hubballi-580 025.

KEB Bill Details for the year 2020-21

Sl. No.	Name of the Building	RR Nos. / A/c No.	April	May	June	July	August	September	October	November	December	January	February	March
1	CDC, DSW, Legal Cell & NSS Sector	26032A / 2077451000	2,614.00	1,589.00	1,704.00	1,986.00	1,914.00	1,734.00	1,628.00	1,446.00	1,576.00	1,834.00	1,528.00	1,771.00
2	New Green House Building	437126 / 6483349550	13,139.00	8,206.00	6,111.00	6,400.00	8,253.00	10,580.00	6,955.00	6,850.00	7,230.00	9,659.00	9,551.00	11,275.00
3	Parasiksha Bhavan	/ 9599801106	7,301.00		26,450.00	60,135.00	10,576.00	11,248.00	12,175.00	11,480.00	13,507.00	12,741.00	15,765.00	16,245.00
4	New Law School Building	HT-383 / 9797263467	28,365.00	33,468.00	34,053.00	34,447.00	37,913.00	32,601.00	33,036.00	31,608.00	36,274.00	37,073.00	33,296.00	35,862.00
5	Ladies Hostel	/ 9581396129	-	-	-	1,13,682.00	-	-	-	-	-	21,717.00	-	-
6	Administrative Building	73074C / 2189851000	-	-	-	70,443.00	-	-	-	-	9,442.00	-	-	-
7	Pump House	MPS809 / 3960061000	4,705.00	3,197.00	1,379.00	1,335.00	-	-	-	-	-	-	-	-
8	KSLU's New Boys Hostel	444684 / 1371922257	-	-	-	-	-	-	-	2,29,144.00	8,394.00	-	59,328.00	43,864.00
9	New Registrar (Adm) Building	/ 0838688869	-	-	-	-	-	-	-	-	9,220.00	-	3,637.00	2,332.00
10	New Registrar (Ev) Building	/ 7682720156	-	-	-	-	-	-	-	-	6,305.00	-	1,795.00	879.00
11	V. C. Residence Building	/ 3259418161	-	-	-	-	-	-	-	-	3,650.00	814.00	907.00	832.00
12	New Teaching Staff Quarters Building	/ 9007326319	-	-	-	-	-	-	-	-	6,230.00	-	2,638.00	1,227.00
		/ 5497012416	-	-	-	-	-	-	-	-	1,705.00	-	503.00	242.00
		/ 1001494804	-	-	-	-	-	-	-	-	1,701.00	-	504.00	242.00
		/ 0301231027	-	-	-	-	-	-	-	-	3,700.00	-	1,566.00	910.00
		/ 0215368281	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		/ 8334333332	-	-	-	-	-	-	-	-	1,705.00	-	503.00	242.00
		/ 8907510044	-	-	-	-	-	-	-	-	1,705.00	-	503.00	242.00
		/ 8134827167	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		/ 1906655375	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		/ 2163832087	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		/ 3569117374	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		/ 9881086905	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		/ 3964071192	-	-	-	-	-	-	-	-	1,705.00	-	501.00	242.00
		Sub Total	56,135.00	44,469.00	69,766.00	2,38,239.00	97,756.00	56,163.00	53,814.00	2,70,528.00	1,24,199.00	83,838.00	1,36,751.00	1,17,819.00
		Grand Total							1,209,418.00					

IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Registrar
Karnataka State Law University
Navanagar, Hubballi-580 025.

KEH BH Details for the year 2022-23

Sl. No.	Name of the Building	BK Nos. / A/c No.	April	May	June	July	August	September	October	November	December	January	February	March
1	CDG, DSW, Legal Cell & NSS Specimen	30032A / 2077451000 407126 / 6483505150	1,229.00	1,300.00	1,125.00	1,281.00	1,280.00	1,810.00	1,560.00	1,911.00	2,675.00	1,695.00	2,130.00	1,852.00
2	New Guest House Building	/ 0506081106	6,758.00	3,999.00	5,400.00	5,492.00	5,278.00	5,802.00	6,085.00	9,680.00	9,833.00	3,100.00	8,325.00	8,640.00
3	Panchajanya Bhavan	HT-583 / 9797043-007	21,708.00	23,375.00	19,351.00	33,348.00	12,600.00	12,372.00	17,465.00	15,994.00	15,517.00	11,514.00	12,228.00	14,840.00
4	New Law School Building	/ 9381396129	38,011.00	34,247.00	38,091.00	40,478.00	41,071.00	38,518.00	37,648.00	39,688.00	48,075.00	37,061.00	48,678.00	43,255.00
5	Ladies Hostel	30074C / 2188851000	37,612.00	23,414.00	50,918.00	-	71,188.00	28,171.00	29,343.00	17,360.00	41,148.00	35,214.00	31,425.00	4,992.00
6	Administrative Building	N/18808 / 560061000	37,232.00	34,986.00	31,046.00	-	88,003.00	95,372.00	44,027.00	34,074.00	31,382.00	24,704.00	13,318.00	52,881.00
7	Pump House	446044 / 2371920237	-	-	50,560.00	-	54,818.00	57,440.00	41,477.00	22,042.00	56,782.00	51,328.00	53,827.00	97,543.00
8	KSLLT's New Boys Hostel	/ 0828688860	2,063.00	1,902.00	1,471.00	1,877.00	1,528.00	1,300.00	2,101.00	1,717.00	2,247.00	1,287.00	1,568.00	1,590.00
9	New Registrar (Adm) Building	/ 368720156	1,167.00	822.00	1,020.00	1,165.00	1,114.00	1,049.00	1,129.00	1,098.00	1,094.00	1,100.00	1,063.00	1,091.00
10	New Registrar (EAO) Building	/ 3250418161	5,148.00	5,148.00	1,627.00	5,895.00	3,410.00	1,585.00	3,610.00	1,582.00	2,187.00	1,415.00	1,553.00	1,497.00
11	V. C. Residence Building	/ 9067328319	3,428.00	3,606.00	5,400.00	3,958.00	3,762.00	4,442.00	2,779.00	2,721.00	5,632.00	2,808.00	4,668.00	4,825.00
12	New Teaching Staff Quarters Building	/ 5497012416	628.00	490.00	470.00	498.00	688.00	563.00	677.00	582.00	714.00	612.00	648.00	1,036.00
		/ 1091494994	328.00	276.00	326.00	338.00	326.00	326.00	320.00	356.00	251.00	320.00	332.00	327.00
		6201231027	321.00	271.00	321.00	321.00	321.00	321.00	320.00	372.00	84.00	527.00	654.00	700.00
		/ 0215948281	331.00	287.00	321.00	331.00	331.00	321.00	316.00	483.00	674.00	481.00	707.00	700.00
		/ 8354333302	804.00	803.00	1,025.00	788.00	993.00	758.00	491.00	418.00	747.00	552.00	681.00	706.00
		/ 8907530044	718.00	800.00	872.00	881.00	803.00	964.00	582.00	504.00	924.00	517.00	801.00	803.00
		/ 8134827107	1,618.00	1,433.00	2,150.00	2,375.00	2,563.00	2,248.00	1,037.00	650.00	2,688.00	1,115.00	2,202.00	1,944.00
		/ 1900633375	558.00	376.00	345.00	338.00	340.00	337.00	505.00	377.00	503.00	483.00	700.00	869.00
		/ 2165832087	331.00	367.00	321.00	328.00	322.00	321.00	320.00	413.00	887.00	573.00	868.00	1,381.00
		/ 3569113774	1,569.00	1,342.00	1,590.00	1,784.00	1,182.00	1,310.00	659.00	474.00	1,259.00	740.00	1,360.00	1,214.00
		/ 881080825	1,041.00	660.00	902.00	948.00	676.00	877.00	476.00	413.00	714.00	517.00	943.00	1,193.00
		/ 3964071192	515.00	499.00	531.00	608.00	585.00	691.00	473.00	463.00	680.00	467.00	588.00	799.00
		Sub Total	2,07,558.00	1,63,619.00	1,94,986.00	1,83,673.00	2,91,213.00	3,17,394.00	1,84,842.00	1,56,386.00	3,27,018.00	1,96,540.00	1,70,299.00	2,82,995.00
		Grand Total							24,79,959.00					

Dayhod
Faculty In-charge

A. Anon
IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Karnataka State Law University
Navanagar, Hubballi-560 025.

Tax Invoice

(ORIGINAL FOR RECIPIENT)

ANJALI ELECTRICALS 207 sar New Anand Nagar, Arjun Nagar, Old-Hubli, Hubli-580024 GSTIN: 29CSUPM2116D22K Contact : 8861319696 E-mail : anjalielectricalshbl@gmail.com		Invoice No. GST-21-22-04	Dated 8-Sep-21
		Delivery Note	Mode/Terms of Payment
		Supplier's Ref	Other Reference(s)
		Despatch Document No.	Delivery Note Date

Buyer The Registrar Karnataka State Law University Navanagar, Dist : Dharwad, Karnataka-29	Despatched through	Destination
	Supply From Place : Anand Nagar, Hubli	Supply To Place : NavaNagar, Dist : Dharwad


Sl. No.	Description of Goods	GST Rate	Quantity	Rate	Per	Amount
ELECTRICAL Bill for Indoor LED Fittings & Street Light						
1	Supply of WIPRO 20watt LED Indoor of 4' feet - LED PVC Batten with intrgrated LED tube standard electrical condition.	12%	120	375.00	Nos	45,000.00
2	Fixing 20watt capacities of LED fluorescent / false ceiling LED fittings indoor on the wall / ceiling.	12%	120	110.00	Each	13,200.00
3	Supply of SYSKA 40w LED Streetlight with pressure die cast aluminum housing body with optimal heat sink.	12%	8	3,360.00	Nos	26,880.00
4	Fixing of 40watt LED Steet light fitting over existing pole / wall ceiling.	12%	8	175.00	Each	1,400.00
Total						86,480.00
5GST 6%						5,188.80
CGST 6%						5,188.80
Round off						0.40
Grand Total						96,858.00

Amount Chargeable (in words) E. & O.E
 INR: Rupees Ninety Six Thousand Eight Hundred and Fifty Eight Only

HSN/SAC	Taxable Value	Central Tax		State Tax		Total Tax Amount
		Rate	Amount	Rate	Amount	
SAC/9954	86,480.00	6%	5,188.80	6%	5,188.80	10,377.60
Total			5,188.80		5,188.80	10,377.60

Tax Amount (in words) : INR: Rupees Ten Thousand Three Hundred Seventy Seven and Sixty Paise only

Company's Bank Details
 Firm Name : Anjali Electricals
 Bank Name : CANARA BANK
 A/C No. : 4206201000092
 Branch Name : Gokul Road, Hubli
 Branch & IFSC code : CNRB0004206

Customer's Seal and Signature	for Anjali Electricals  Authorised Signatory
-------------------------------	---

SUBJECT TO HUBLI JURISDICTION

This is a Computer Generated Invoice


IQAC COORDINATOR
 Karnataka State Law University
 Hubballi-25.


Registrar
 Karnataka State Law University
 Navanagar, Hubballi-580 025.

2013-14

Name of Work : Construction of RCC Sump at Boys Training Hostel for KSLU, Navanagar, Hubli
Agency : Shri. V. D. Damanal, Contractor, Hubli

R A BILL First and Final

MB No. 2127 Page No. 98 to 105

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
1	KSRB 2-2.2: Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5 m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. SR Page-05/2.4 (Earthwork excavation)	Cum	194.48	54.58	10,615.00	-	-	54.58	10,615.00
2	KSRB 4-1.6: Providing and laying in position plain cement concrete of mix M15 with OPC cement @ 240 Kgs, with 20 mm and downsize graded granite metal course aggregates @ 0.878 cum and fine aggregates @ 0.459 cum, machine mixed, concrete laid in layers not exceeding 15 cms thick, well compacted, in foundation, plinth and sills, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. SR Page - 12 / 4.6	Cum	4843.28	5.36	25,960.00	-	-	5.36	25,960.00
3	KSRB - 6-1.3: Providing and constructing burnt brick masonry for basement and superstructure with approved quality of non-modular bricks of standard size of class designation 35 with cement mortar 1:6 including cost of materials, labour charges, scaffolding, curing complete as per specifications. SR Page - 30/6.3 (BBM)	Cum	3970.72	12.64	50,190.00	-	-	12.64	50,190.00
4	KSRB 15-3.2: Providing 18 mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering. : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. SR Page -121/15.16	Sqin	166.40	56.50	9,402.00	-	-	56.50	9,402.00
5	KSRB -2.5: Earthwork excavation (in deposited soil) and filling sides of foundation upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with all lead and lift including cost of all labour complete as per specifications. SR Page -06/2.12 (Basement filling)	Cum	173.68	16.24	2,821.00	-	-	16.24	2,821.00

(Signature)

IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Karnataka State Law University
Navanagar, Hubballi-580 025.

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
6	KSRRB 4-2.2: Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 320 kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregates @ 0.459 cum, with superplasticiser @ 3 ltrs conforming to IS9103-1999 Renaffimede-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation plinth and ground floor level for roof slabs, staircase, fireles, retaining walls, return walls, walls (any thickness) including attached plasters, columns, piers, abutments, pillars, posts, struts, buttresses, string or facing courses, parapets, coping, bed blocks, anchor blocks, plain window cills, fillets etc., including costs of all materials, labour, HDM of machinery, curing, complete as per specifications. SR Page -13/4,11 (RCC Works)	Cum	5534.88	18.09	100,126.00	-	-	18.09	100,126.00
7	KSRRB 4-6.4: Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, including attached plasters, buttresses, plinth and string courses cost of all materials labour complete as per specifications. SR Page -17/4,31 (Centering for RCC Retaining Wall)	Sqm	234.00	44.66	10,450.00	-	-	44.66	10,450.00
8	KSRRB 4-6.2 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for flat surface such as suspended floors, roofs, landings, balconies and like, thickness upto 200 mm including cost of all materials, labour complete as per specifications. SR Page -16/4,29 (Centering for Roof Slab)	Sqm	248.56	21.22	5,274.00	-	-	21.22	5,274.00
9	KSRRB 4-6.7: Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for sides and soffits of beams, beams haunchings, cantilever girders, bressures and lintels not exceeding 1m in depth including cost of all materials, labour complete as per specifications. SR Page -17/4,34 (Centering for Roof Beam)	Sqm	213.20	4.69	1,000.00	-	-	4.69	1,000.00
10	KSRRB 19-4.9.2: Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HDM of machinery complete as per specifications. SR Page -19/4,46 (TMT Steel)	Qtl	7265.44	11.56	83,988.00	-	-	11.56	83,988.00

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
11	KSRB 15-3.2: Providing 18 mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering. : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. Extra for providing and mixing waterproofing compound in cement plaster work in at one kg per bag or in the proportion recommended by the manufacturers, for cement mortar 1:4, 18mm thick coat of materials as per specifications. Providing floating coat of cement plaster to plastering and finishing smooth, including cost of materials, labour, curing complete as per specifications. SR Page 121/15.16,15.26,15.32 (Plastering with Water proofing Compound and Cement finish inside)	Sqm	190.01	67.22	12,772.00	-	-	67.22	12,772.00
12	KSRB 7.9 : Providing and fixing M.S. grill work for windows and ventilators weighing 21 kg/sqm using M.S. flats, or M. S. square rods, or combination of M.S. flats and square rods as per approved design, drawing including cutting steel sections and welding the same to required pattern with a coat of red lead primer, cost of materials, fixtures, labour and HOM of machinery complete as per specifications. SR Page-377.9 (M.S. Grill)	Kgs	90.48	35.00	3,167.00	-	-	35.00	3,167.00
	Total				315,765.00				315,765.00


Asst. Ex. Engineer
KSLU, Hubli


Asst. Engineer
KSLU, Hubli


Resident Engineer
KSLU, Hubli


Contractor:


IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.


Registrar

Karnataka State Law University
Navanagar, Hubballi-580 025.

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
11	KSRB 15-3.2: Providing 18 mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including coat of materials, labour, curing complete as per specifications. Extra for providing and mixing waterproofing compound in cement plaster work in at one kg per bag or in the proportion recommended by the manufacturers, for cement mortar 1:4, 18mm thick coat of materials as per specifications. Providing floating coat of cement plaster to plastering and finishing smooth , including cost of materials, labour, curing complete as per specifications. SR Page 123+124/15.16,15.26,15.32 (Plastering with Water proofing Compound and Cement finish Inside)	Sqm	216.49	118.97	25,755.00	-	-	118.97	25,755.00
12	KSRB 7.9 : Providing and fixing M.S. grill work for windows and ventilators weighing 21 kg/sqm using M.S. flats, or M. S. square rods, or combination of M.S. flats and square rods as per approved design, drawing including cutting steel sections and welding the same to required pattern with a coat of red lead primer, cost of materials, fixtures, labour and HOM of machinery complete as per specifications. SR Page-377.9 (M.S. Grill)	Kgs	91.80	70.00	6,426.00	-	-	70.00	6,426.00
	Total				486,547.00				486,547.00

Dudappa
Asst. Engineer
KSLU, Hubli

V.S.
Asst. Ex. Engineer
KSLU, Hubli

S.L. Sarwan
Resident Engineer
KSLU, Hubli

A. S. S.
IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Devgod
Registrar
Karnataka State Law University
Navanagar, Hubballi-580 025,

20/11/15

22

Name of Work : Construction of Septic Tank and Repairing Sanitary Pipelines at Boys Training Hostel at KSLU Premises, Navanagar, Hubli

Agency : Shri. C. H. Kattimani, Hubli

R A BILL First and Final

MB No. 2130 Page No. 96 to 102

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
1	KSRB 2-2.2: Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5 m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. SR Page-05/2.4	Cum	224.64	40.44	9,084.44	-	-	40.44	9,084.44
2	(Earthwork excavation) KSRB 5-14 : Providing and constructing precast concrete solid blocks with compressive strength not less than 35 kg/Sqm with cement mortar 1:4 masonry (quoin, jamb, closer blocks) with solid concrete blocks of size 40x20x20 cms conforming to I.S : 2185 / 1965 in superstructure including cost of materials, labour charges, scaffolding, curing complete as per specifications. SR Page -27 / 5.27 (Concrete Blocks)	Sqm	856.44	22.26	19,064.35	-	-	22.26	19,064.35
3	KSRB 12-1.1 : Providing and laying in position to required level or slope 100mm internal diameter salt glazed stoneware pipes grade A and jointing with stiff mixture of cement mortar in proportion of 1:1 testing of pipes and joints, including cost of materials, labour charges complete as per specifications. SR Page - 72/11.1 (Stoneware Pipes)	Mtr	225.72	36.00	8,125.92	-	-	36.00	8,125.92
4	KSRB 15-3.9: Providing 18mm thick cement plaster in single coat with cement mortar 1:6, to brick masonry including rounding off corners wherever required smooth rendering. : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. SR Page -122/15.17 (Plastering)	Sqm	167.40	7.98	1,335.85	-	-	7.98	1,335.85

Signature



Registrar
Karnataka State Law University
Navanagar, Hubballi-580 025.

Signature
IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
5	KSRB 14.10-3: Providing flooring with 25 mm to 40 mm thick polished Cadapa Slabs using cement mortar 1:6, 25mm thick over existing cement concrete bed or top of roof laid to line and level and jointed with cement slurry mixed with pigment to match the shade of the slab, including cost of materials, labour, curing, polishing complete as per specifications. SR Page - 112 / 14.17 (Cadapa Slabs)	Sqm	1034.64	10.26	10,615.41	-	-	10.26	10,615.41
6	KSRB -2.5: Earthwork excavation (in deposited soil) and filling sides of foundation upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with all lead and lift including cost of all labour complete as per specifications. SR Page -06/2.12 (Earth filling)	Cum	200.88	25.10	5,042.09	-	-	25.10	5,042.09
7	KSRB 13-9-3: Providing and fixing to wall, ceiling and floor high density polyethylene pipes 6.00 kg/bsq.cm working pressure 75mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor, including cost of all materials, labour charges, HOM of equipments and testing complete as per specifications. SR Page 102/13.73 (PVC Pipes)	Mtr	421.20	35.25	14,847.30	-	-	35.25	14,847.30
8	KSRB 12-8.1 : Constructing brick masonry inspection chamber 450x450mm and 450mm depth (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, (excluding C.I Cover with frame (light duty) 450x450mm internal dimensions, total weight of cover with frame to be not less than 38 kg (weight of cover 23kg and weight of frame 15kg)) R.C.C top slab with cement concrete M15 with 20mm and downsize granite metal, foundation concrete M5 with 40mm and downsize granite metal inside plastering 12mm thick with cement mortar 1:3, finish smooth with a floating coat of cement on walls and bed concrete complete as per standard design including cost of materials, labour charges, curing complete as per specifications. SR Page 75/11.50.2 Note: Item excluding CI cover rate is arrived by deducting cost of CI Cover.	Nos	2350.04	1.00	2,350.04	-	-	1.00	2,350.04

2

20

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
9	KSRB 12-8.2 : Constructing brick masonry inspection chamber 500x700mm and 450mm depth (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, (excluding C.I Cover with frame (light duty) 455x610mm internal dimensions, total weight of cover with frame to be not less than 38 kg (weight of cover 23kg and weight of frame 15kg)) R.C.C top slab with cement concrete M15 with 20mm and downsize granite metal, foundation concrete M5 with 40mm and downsize granite metal inside plastering 12mm thick with cement mortar 1:3, finish smooth with a floating coat of cement on walls and bed concrete complete as per standard design including cost of materials, labour charges, curing complete as per specifications. SR Page 76/11.52 Note: Item excluding CI cover rate is arrived by deducting cost of CI Cover.	Each	4915.04	1.00	4,915.04	-	-	1.00	4,915.04
10	Scavengers for cleaning of Septic Tank and removing of old existing broken Sanitary Pipelines. SR Page - XLIX/10	Nos	193.38	24.00	4,641.12	-	-	24.00	4,641.12
Total					80,021.56				80,021.56

[Signature]

Contractor

[Signature]
Asst. Engineer
KSLU, Hubli

[Signature]
Asst. Ex. Engineer
KSLU, Hubli

[Signature]
Resident Engineer
KSLU, Hubli

[Signature]
Registrar

Karnataka State Law University
Navanagar, Hubbleli-580 025.

[Signature]
IQAC COORDINATOR
Karnataka State Law University
Hubbleli-25.

7.1.4 Water Conservation Facilities available in Karnataka State Law University

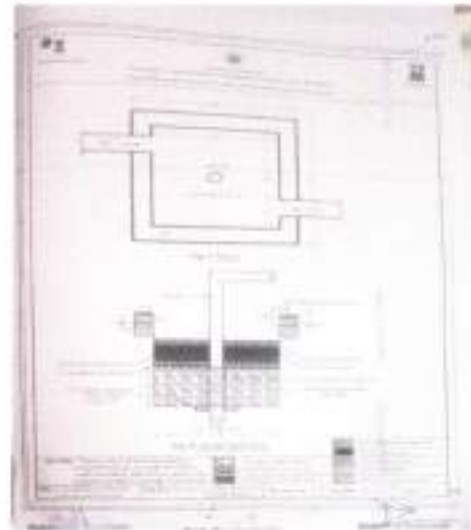
1. Rain Water Harvesting:

Rain Water Harvesting work has been undertaken in the premises of Administrative Building and Ladies Hostel of the Karnataka State Law University. The Rain water collected in the Administrative building and Ladies hostel campus and roof top is collected in a tank through pipelines and this water is in turn used to recharge the borewells and the ground water.(Photos are Enclosed)

2. Borewell / open well recharge:

Borewell recharge works are being taken up in the following locations of Karnataka State Law University. (Photos are Enclosed)

1. Borewell near Administrative Building
2. Borewell near Vice Chancellor Residence
3. Borewell Near Boy's Hostel
4. Borewell Near Teaching Staff Quarters
5. Registrar (Evaluation) Bunglow
6. Borewell between Boy's and Ladies Hostel.





Borewell Recharge Near Boy's Hostel

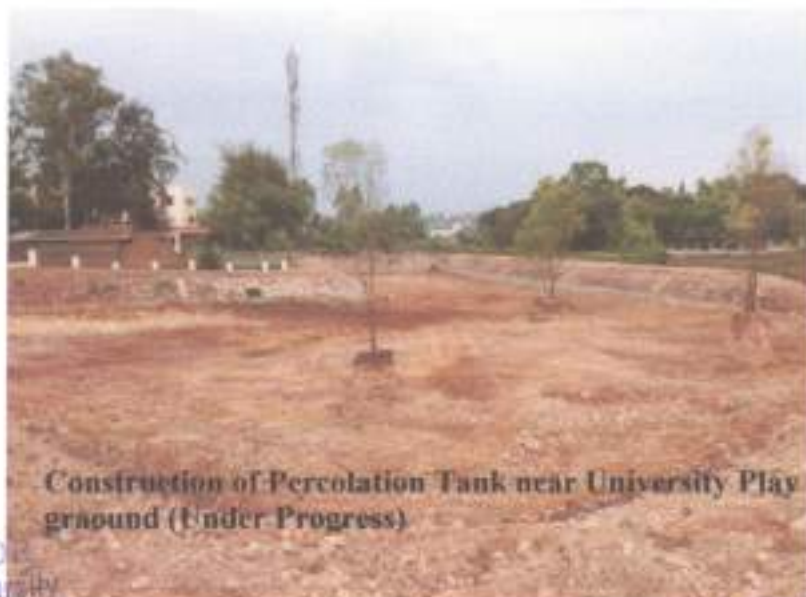
Construction of Tanks and bunds:

Construction of Check dam to store the Rain water is under progress near Teaching Staff Quarter's Building by Minor Irrigation Department



Construction of Checkdam near Teaching staff Quarters (Under Progress)

Construction of Percolation tank to recharge the ground water is under progress Near University Play Ground by Minor Irrigation Department



Construction of Percolation Tank near University Play ground (Under Progress)

A. Rao
IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Ajshree
Registrar
Karnataka State Law Univer
Nayanagar, Hubballi-580 0

2017-18

FORM P.W.G.33 (C) . I. Accounts of works Executed

RA Bill No: Ist and Part Final

Technical Sanction Estimate No : RE/8 for 02/2017 Dated: 16.02.2017

Name of Work : Providing Rain Water Harvesting to Karnataka State Law University Buildings, KSLU Premises, Navanagar, Hubballi

Agency : Shri. Kumar H. B., Dharwad

Agr No: Tend/03/26.05.2017

Item No.	Tender Quantity	Description	Unit	Rate	Upto Date		Previously Paid		Now to be Pay		
					Qty	Amount	Qty	Amount	Qty	Amount	
1	2	3	4	5	6	7	8	9	10	11	
1	61.722	KSRB 2-1.2 : Earthwork in surface excavation in Hard soil for levelling and lowering the ground manually (other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to a distance not exceeding 50m and lift upto 1.5m, excavated surface levelled and neatly dressed, disposed earth to be levelled after breaking of clods and neatly dressed as per specifications. specification. No. KBS 2.1(a) / 2.3.1 Note : Adopt item 2.24 for excavation in all types of soils for lowering & levelling the ground for building works by mechanical means KSRB 2-2.2 : Earthwork excavation by manual means for foundation of buildings, culverts, water supply and sanitary lines and electrical conduits etc, either in pits or in trenches 1.5m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. including breaking of clods complete as per specifications. No. KBS 2.1(a) / 2.3.5	cum	204.0	90.88	18540.00	-	-	90.88	18540.00	
2	56.727	KSRB 4-1.3 : Providing and laying in position plain cement concrete of mix 1:4:8 with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregates @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4.1, 4.2	cum	239.0	56.7	13551.00	-	-	56.70	13551.00	
3	4.026		cum	4405.0	2.44	10748.00	-	-	2.44	10748.00	

IOAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Karnataka State Law University
Navanagar, Hubballi-580 025.

Item No.	Tender Quantity	Description	Unit	Rate	Upto Date		Previously Paid		Now to be Pay	
					Qty	Amount	Qty	Amount	Qty	Amount
1	2	3	4	5	6	7	8	9	10	11
4	15.8355	KSRB 5.1.3 : Providing and constructing granite / trap / basalt rubble stone masonry in foundation with cement mortar 1:6 (uncoursed), bond stones at two m. apart in each course including cost of materials, labour, curing complete as per specifications. KBS 5.1.12	cum	2750.0	16.26	44715.00	-	-	16.26	44715.00
5	2.5872	KSRB 4.1.7 : Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.84cum and fine aggregates @ 0.56cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, H.O.M of machinery, curing complete as per specifications.	cum	4770.0	2.33	11114.00	-	-	2.33	11114.00
6	33.12	Specification No. KBS 4.1.4.2 KSRB 15.1.4 Providing ruled pointing to coursed stone masonry with cement mortar 1:4, 20mm deep, after raking joints to depth of 20mm nicely lining, including cost of materials, labour, curing complete as per specifications.	Sqm	83.0	28.64	2377.00	-	-	28.64	2377.00
7	56.7	KSRB 2.8 : Providing and Filling in foundation with granite / trap broken metal materials, labour, curing complete as per specifications. KSRB 2.2.7 : Earthwork excavation by manual means for foundation of buildings, culverts, water supply and sanitary lines and electrical conduits etc, either in pits or in trenches 1.5m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. including breaking of clods complete as per specifications. No. KBS 2.1(a) / 2.3.5	cum	1676.0	56.55	94778.00	-	-	56.55	94778.00
8	97.125		cum	242.0	98.14	23750.00	-	-	98.14	23750.00

IQAC COORDINATOR

Karnataka State Law University

Hibbhall-25.

Item No.	Tender Quantity	Description	Unit	Rate	Upto Date		Previously Paid		Now to be Pay	
					Qty	Amount	Qty	Amount	Qty	Amount
1	2	3	4	5	6	7	8	9	10	11
9	259	Providing and fixing to wall, ceiling and floor unplasticised PVC pipes 10.00 kg/94cm working pressure chemp plast / Wavin or equivalent make with pipe fittings, wall clips, making good the wall, ceiling and floor, including cost of all materials, with 160mm outer dia	M	1232.0	259	319088.00	-	-	259.00	319088.00
10	93.0921	KSRB 2-4 : Refilling available earth around pipe lines, cables in layers not exceeding 20cms in depth, compacting each deposited layer by ramming after watering with lead upto 50m and lift upto 1.5 m. including cost of all labour complete as per specifications.	cum	53.0	59.32	3144.00	-	-	59.32	3144.00
Total						541805.00	-	-		541805.00


Jr. Engineer
 KSLU Navanagar Hubli.


Assistant Executive Engineer,
 KSLU Navanagar Hubli.


Resident Engineer,
 KSLU Navanagar Hubli.

X

 IQAC COORDINATOR


IQAC COORDINATOR
 Karnataka State Law University
 Hubballi-25.


 Professor
 Karnataka State Law University
 Navanagar, Hubballi-580 025 -

2017-18

Name of Work : Construction of RCC Sump at Guest House at KSLU Premises, Navanagar, Hubballi

M. B. No. 2143 Page No. 12 to 33

Name of the Agency : Shri. Manjunath Ganiger, Dharwad

RA Bill I and Final

Item No	Item of work	Unit	Rate	Tendered Qty	Up to date		Previous		Since Previous	
					Qty	Amount	Qty	Amount	Qty	Amount
1	KSRB 2-2.2 : Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. No. KBS 2.1(b)/2.3.5	cum	255.67	31.00	38.51	9,845.85	-	-	38.51	9,845.85
2	KSRB 4-1.3 : Providing and laying in position plain cement concrete of mix 1:4:8 with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregates @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4.1, 4.2	cum	4874.25	3.90	6.59	32,121.31	-	-	6.59	32,121.31
3	KSRB 4-1.6 : Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregates @ 0.459cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4.1, 4.2	cum	5438.47	2.40	2.28	12,399.71	-	-	2.28	12,399.71
4	KSRB 5.1-3 : Providing and constructing granite / trap / basalt rubble stone masonry in foundation with cement mortar 1:6 (uncoursed), bond stones at two m. apart in each course including cost of materials, labour, curing complete as per specifications.KBS 5.1.12	cum	2757.68	8.90	9.47	26,115.23	-	-	9.47	26,115.23

Signature
Rajaram

Signature
IQAC COORDINATOR
Karnataka State Law University
Hubballi-25.

Karnataka State Law University
Navanagar, Hubballi-560 025

Item No	Item of work	Unit	Rate	Tendered Qty	Up to date		Previous		Balance	
					Qty	Amount	Qty	Amount	Qty	Amount
5	KSRB 4.2.1 : Providing and laying in position reinforced cement concrete of Design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0.70 cum and fine aggregates @ 0.47cum, with super plasticiser @ 3 liters confirming to IS 9103-1999 rebarred-2008 at machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation for footings, pedestals, retaining walls, return walls, walls (any thickness) including attached pilasters, columns/pillars, posts, struts, buttresses, bed blocks, anchor blocks & plinths etc., including cost of all materials, labour, HOM of machinery, curing, complete but excluding cost of reinforcement as per specifications. Specification No. KBS 4.1.4.6	cum	6242.99	10.20	11.18	69,796.63	-	-	11.18	69,796.63
6	KSRB 4.2.10 : Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 24kgs, with 12mm and down size graded granite metal coarse aggregates @0.05175cum and fine aggregates @ 0.0345cum, with superplasticiser @0.225lit, machine mixed, well compacted for plain chajin of 7.5 cms. average thickness, upto ground floor level, including cost of all materials, labour, HOM of machinery, finishing, curing, complete but excluding cost of reinforcement as per specifications. Specification No. KBS 4.1.4.6	Sqm	456.57	4.25	4.48	2,045.43	-	-	4.48	2,045.43
7	KSRB 4-6.14 Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for sloping or horizontal surface including folded plates where inclination to horizontal plane does not exceed 30 degree requiring shuttering only on the under side including cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2	Sqm	382.55	4.25	4.48	1,713.82	-	-	4.48	1,713.82
8	KSRB 4-6.4 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, including attached pilasters, buttresses, plinths and string courses cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2	Sqm	269.13	51.00	50.40	13,564.15	-	-	50.40	13,564.15

Item No	Item of work	Unit	Rate	Tendered Qty	Up to date		Previous		Since Previous	
					Qty	Amount	Qty	Amount	Qty	Amount
9	KSRB 4-6.2 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for flat surface such as roofs, landings, balconies and likes, thickness upto 200 mm including cost of all materials, labour complete as per specifications up to 3.50m from Ground level. Specification No. KBS 4.6.2	Sqm	283.55	22.20	22.13	6,274.96	-	-	22.13	6,274.96
10	KSRB 4-6.7 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for sides and soffits of beams, beam haunchings, cantilever girders, bressumers and lintels not exceeding 1m in depth including cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2	Sqm	237.41	7.00	2.82	669.50	-	-	2.82	669.50
11	KSRB 4.9.2 : Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, booking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, H.O.M of machinery complete as per specifications. Specification No. KBS 4.6.3 - TMT bars Fe 500	MT	58955.2	0.90	1.05	61,902.96	-	-	1.05	61,902.96
12	KSRB 6-1.3 : Providing and constructing burnt brick masonry for basement and superstructure with approved quality of non-modular bricks of standard size of class designation 3.5 Newton per sqmm with cement mortar 1:6 including cost of materials, labour charges, scaffolding, curing complete as per specifications. Specification No. KBS 6.2	cum	4880.97	5.10	5.00	24,404.85	-	-	5.00	24,404.85
13	KSRB15-3.2 : Providing 12mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.	Sqm	150.9	25.60	29.09	4,389.68	-	-	29.09	4,389.68
14	KSRB15-3.8 : Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.	Sqm	201.85	32.50	36.64	7,395.78	-	-	36.64	7,395.78

Signature
 P. S. SURESH

IQAC COORDINATOR
 Karnataka State Law University
 Hubballi-25.

Karnataka State Law University
 Navanagar, Hubballi-580 002
 January

Item No	Item of work	Unit	Rate	Tendered Qty	Up to date		Previous		Since Previous	
					Qty	Amount	Qty	Amount	Qty	Amount
15	KSRB 15-15.1 : Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, complete as per specifications. - with primer	Sqm	86.5	25.60	31.70	2,742.05	-	-	31.70	2,742.05
16	Providing and finishing external walls in two coats over one coat of primer with antifungal paint of approved brand and shade to give an even shade after thoroughly brooming the surface to remove all dirt and loose powdered material, free from mortar drops and other foreign matter cost of materials, labour, complete as per specifications.	Sqm	140.33	32.50	36.98	5,189.40	-	-	36.98	5,189.40
17	KSRB15-3.8 : Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth removing scaffolding, including cost of materials, labour, curing complete as per specifications.	Sqm	201.85	30.00	29.75	6,005.04	-	-	29.75	6,005.04
18	KSRB15-4.4 Extra for providing and mixing waterproofing compound in cement plaster work at one kg per bag or in the proportion recommended by the manufacturer, for cement mortar 1:4, 18mm thick coat of materials complete as per specifications.	Sqm	8.12	30.00	29.75	241.57	-	-	29.75	241.57
19	KSRB15-6 : Providing floating coat of cement to plastering and finishing smooth, including cost of materials, labour, curing complete as per specifications.	Sqm	18.16	30.00	29.75	540.26	-	-	29.75	540.26
20	C1 mashaole cover with frame 610x455mm size (38 Kgs)	Each	1958.0	1.00	1.00	1,958.00	-	-	1.00	1,958.00

Item No	Item of work	Unit	Rate	Tendered Qty	Up to date		Previous		Since Previous	
					Qty	Amount	Qty	Amount	Qty	Amount
21	KSRB 7.10 : Providing and fixing in position aluminium windows and ventilators as per approved drawings with sliding shutters using double track window frame section of size 61.85x31.75mm. with 1.2mm thick, bottom section weight 0.695 kg/m, slides and top sections 1.3 mm. thick weight 0.659 kg/m; and shutter comprising top and bottom section of size 40mmx18mm, 1.25mm thick 0.417 kg/m; shutter outer side 40mmx18mm, 1.25mm.thick weight 0.417 kg/m, shutter inter-lock section 40mmx26.7mm, 1.1mm thick, weight 0.469 kg/m. the shutters mounted on nylon rollers with approved quality of fixtures such as aluminium handles (lower bolts etc.); and providing and fixing 5.5mm. thick plain glass for shutters fitted with rubber beading aluminium sections including cutting to required length, joints mitred subdividing the frame tenoned and rivetted in the assembled frame stiffened with end clips at corners angles etc., and fixed to the walls, lintels, floor beams/cells as the case may be with necessary steel screws, raul plugs, or teak wood gatties including cutting masonry or concrete and making good the original surface using cement mortar, aluminium sections pretreated for removal of any Specification No. KBS	Sqm	3663.1	5.22	5.15	18,864.97	-	-	5.15	18,864.97
22	KSRB 7.9 : Providing and fixing M.S.grill work for windows and ventilators weighing 21kg/sqm using M.S. flats, or M.S. square rods, or combination of M.S. flats and square rods as per approved design, drawing including cutting steel sections and welding the same to required pattern with a coat of red lead primer, cost of materials, fixtures, labour and HOM of machinery complete as per specifications. Specification No. KBS.7.12	kgs	87.46	131.00	128.75	11,260.48	-	-	128.75	11,260.48
23	Providing vitrified tiles 60 x 60cms of approved make, shade and size for flooring laid on a bed of 12mm thick cement mortar 1:3 mix, flush pointing with white cement using colour pigment, including cost of materials, labour, curing complete as per specification.	Sqm	1027.52	6.10	7.96	8,179.06	-	-	7.96	8,179.06
24	KSRB 9.4-3 : Providing Masfai / Nandi wood frames of doors, windows, clerestory windows, ventilators and other frames, wrought, framed or assembled including making plaster grooves (excluding cost of cement concrete and side clamps), but including cost of materials, labour, HOM of machineries complete as per specifications. Specification No. KBS.9.33	cum	56224.4	0.05	0.051	2,867.44	-	-	0.051	2,867.44

Signature

Since Previous Amount
11,260.48

Up to date Amount
18,864.97

Previous Amount
-

Since Previous Amount
18,864.97

Up to date Amount
11,260.48

Previous Amount
-

Since Previous Amount
2,867.44

[Signature]

Item No	Item of work	Unit	Rate	Tendered Qty	Up to date		Previous		Since Previous	
					Qty	Amount	Qty	Amount	Qty	Amount
25	Providing and fixing flush door shutter made out of solid core black board type, well seasoned chemically treated hard wood battens and internal frame with minimum 45 mm wide wooden frame all-round door shutters covered with cross bonded wooden sheets (core veneer) hot pressed and fastened on both sides of the door using liquid phenol formaldehyde resin as per IS specification 2202 (Part-1) 1991. From manufacturer (Factory) complete as per specification. - 30mm thick both side commercial	Sqm	1921.44	1.89	1.88	3,612.31	-	-	1.88	3,612.31
26	KSRB 15-17.1 : Applying priming coat over new wood surface and / or wood based surface with white lead paint priming including preparing the surface after thoroughly cleaning oil, grease, dirt and foreign matter, sand papering and knotting ready mix paint including cost of materials, labour, complete as per specifications.	Sqm	29.79	3.78	3.91	116.48	-	-	3.91	116.48
27	KSRB 15-17.6 : Providing and applying painting two coats (excluding priming coat) on new wood surface and / or wood based surface with enamel paint to give an even shade, cleaning the surface of all dirt, dust and foreign matter, sand papering including cost of materials, labour, complete as per specifications.	Sqm	76.89	3.78	4.34	333.70	-	-	4.34	333.70
28	Handles power coated 150 mm	Each	49.84	2.00	2.00	99.68	-	-	2.00	99.68
29	Hinges 5" heavy duty	Each	32.93	3.00	3.00	98.79	-	-	3.00	98.79
30	Locking system	No.	890.0	1.00	1.00	890.00	-	-	1.00	890.00
31	KSRB 15-18.2 : Providing and applying enamel metal paint two coats (excluding priming coat) over new steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost of materials, labour, complete as per specifications.	Sqm	74.97	5.50	5.22	391.34	-	-	5.22	391.34
				Total		336,030.00				336,030.00

[Signature]
Contractor

[Signature]
**Asst. Engineer
KSLU, Hubli**

[Signature]
**Asst. Ex. Engineer
KSLU, Hubli**

[Signature]
**Resident Engineer
KSLU, Hubli**

2,867.44

20/14-15

Name of Work : Construction of RCC Sump at KSLU Campus, Near Administration Building, Navanagar, Hubli.
 Agency : Shri. V. D. Damana, Contractor, Hubli

R A BILL First and Final

MB No. 2135 Page No. 96 to 103

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
1	KSRB 2-2.2: Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5 m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. SR Page-05/2.4 (Earthwork excavation)	Cum	224.64	145.65	32,719.00	-	-	145.65	32,719.00
2	KSRB 4-1.6 : Providing and laying in position plain cement concrete of mix M15 with OPC cement @ 240 Kgs, with 20 mm and downsize graded granite metal course aggregates @ 0.878 cum and fine aggregates @ 0.459 cum, machine mixed, concrete laid in layers not exceeding 15 cms thick, well compacted, in foundation, plinth and sills, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. SR Page - 12 / 4.6	Cum	5175.36	6.34	32,812.00	-	-	6.34	32,812.00
3	KSRB - 6-1.3: Providing and constructing burnt brick masonry for basement and superstructure with approved quality of non-modular bricks of standard size of class designation 35 with cement mortar 1:6 including cost of materials, labour charges, scaffolding, curing complete as per specifications. SR Page - 30/6.3 (BBM)	Cum	4790.88	19.31	92,512.00	-	-	19.31	92,512.00
4	KSRB 15-3.2: Providing 18 mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering. : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. SR Page -123/15.16	Sqm	190.08	95.84	18,217.00	-	-	95.84	18,217.00
5	KSRB -2.5: Earthwork excavation (in deposited soil) and filling sides of foundation upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with all lead and lift including cost of all labour complete as per specifications. SR Page-06/2.12 (Basement filling)	Cum	200.88	19.12	3,841.00	-	-	19.12	3,841.00

Signature
 Registrar

Item No	Item of work	Unit	Rate	Up to Date		Previous Paid		Since Previous	
				Qty	Amount	Qty	Amount	Qty	Amount
6	KSRB 4-2.2: Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 320 kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregates @ 0.459 cum, with superplasticiser @ 3 ltrs conforming to IS9103-1999. Ready-mix concrete-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation plinth and ground floor level for roof slabs, staircase, lintels, retaining walls, return walls, walls (any thickness) including attached plasters, columns, piers, abutments, pillars, posts, struts, buttresses, string or facing courses, parapets, coping, bed blocks, anchor blocks, plain window cills, fillets etc., including costs of all materials, labour, HOM of machinery, curing, complete as per specifications. SR Page -13/4.11 (RCC Works)	Cum	5937.84	25.15	149,337.00	-	-	25.15	149,337.00
7	KSRB 4-6.4: Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, including attached plasters, buttresses, plinth and string courses cost of all materials labour complete as per specifications. SR Page -17/4.31 (Centering for RCC Retaining Wall)	Sqm	267.84	64.85	17,369.00	-	-	64.85	17,369.00
8	KSRB 4-6.2 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for flat surface such as suspended floors, roofs, landings, balconies and like, thickness upto 200 mm including cost of all materials, labour complete as per specifications. SR Page -16/4.29 (Centering for Roof Slab)	Sqm	281.88	28.14	7,932.00	-	-	28.14	7,932.00
9	KSRB 4-6.7: Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for sides and soffits of beams, beams haunchings, cantilever girders, bressumers and lintels not exceeding 1m in depth including cost of all materials, labour complete as per specifications. SR Page -17/4.34 (Centering for Roof Beam)	Sqm	244.08	2.42	591.00	-	-	2.42	591.00
10	KSRB 19-4.9.2: Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications. SR Page -19/4.46 (TMT Steel)	Qd	7374.24	13.43	99,036.00	-	-	13.43	99,036.00

R
